

# CPC Renovation Daily Diary

## Week Ten

Updated Last  
Wednesday – January 6, 2010


### Monday – January 5, 2010

The New Year started with a new sub-contractor on site Monday. The railings that will support the movable walls in Fellowship Hall were being installed. Also today the supports were removed in the northwest corner of Fellowship Hall and the room is now completely open.



### Tuesday – January 6, 2010

We had both the structural engineer (Wes Harrison) and our architectural firm representative (Jim Hooker) on site today to inspect the steel supports in Fellowship Hall and the proposed new entry into the Sanctuary. They also discussed the railing system for the movable walls in Fellowship Hall and the ramp construction what will lead from the new elevator to the Sanctuary. There were several additional activities today as the roof was cut open above the new elevator shaft and holes were cut in the floor between the first and second floor in the office, class room area. The HVAC workers are preparing the new heating/air conditioning vents and with that additional dust in every area of the building. The masons were back finishing the entry doors into the new restroom areas along with the filing in above the steel in Fellowship Hall. The demolition crew opened the new window into the pastor's office. With the temperature outside in the teens the church can become cool quickly.

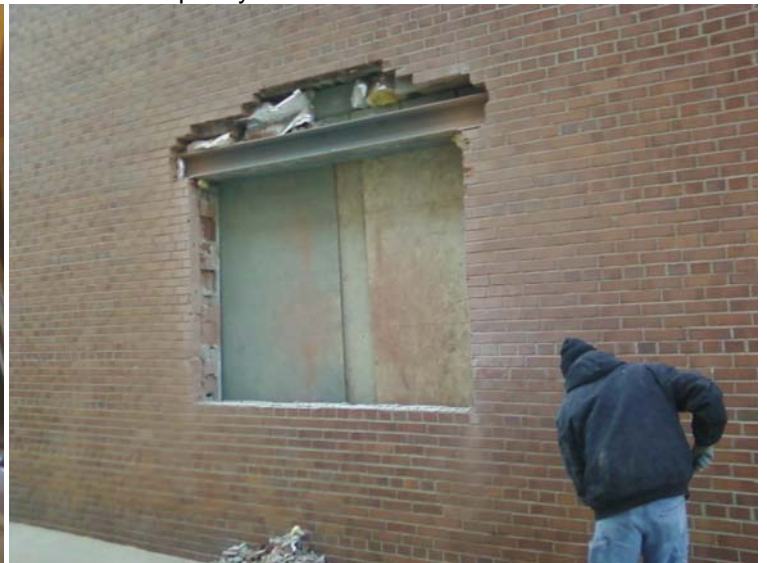

The demolition crew opening the new window in the pastor's office.

# CPC Renovation Daily Diary

## Week Ten

Updated Last  
Wednesday – January 6, 2010



Picture shows the holes being cut into the roof above new elevator shaft and the enclosure on roof so the brick layers and roofers can finish the elevator installation and keep the weather out.



HVAC crew cutting the holes between the first and second floors to make the openings for the new heating and air conditioning vents.

### Wednesday – January 7, 2010

The masons worked on the elevator shaft by placing blocks above the roof cut in the wooden enclosure that was built yesterday. The HVAC workers are concentrating on finishing the work in Fellowship Hall along with the electrician so that the carpenters can frame the wall and then we can have the drywall attached. The plumbers were cutting the trenches necessary to get drains to the new sinks in the pre-school room, nursery, and new upstairs restroom that will be built in the old choir room. There was no formal meeting with the contractors today.

# CPC Renovation Daily Diary

## Week Ten

Updated Last

Wednesday – January 6, 2010



The five air conditioning/heating unit encasements that will be placed on the roof were delivered today. Also the cement pad that will support the transformer in the electrical room was poured.



Thursday – January 8, 2010

Friday – January 9, 2010
