


CPC Renovation Daily Diary

Week Four

Updated Last
Wednesday November 18, 2009

Tuesday – November 17, 2009

The plumbers worked on the new drains and water lines for the new pre-school and new upstairs restrooms. Demolition continued to clean up the new elevator pit before the cement floor is poured on Wednesday. The Pipe Workers were here today for the first time to start removal of the old boiler pipes that surround the walls on the first floor in the Sunday school addition.

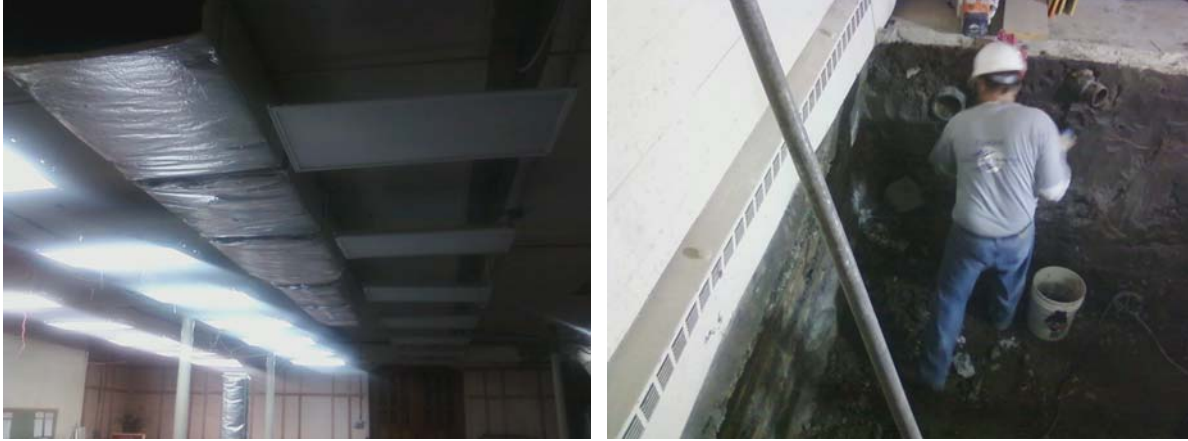

New duct work in Fellowship Hall and elevator pit preparation

Wednesday – November 18, 2009

Ideal Metal Works started hanging the new heating duct work in Fellowship Hall. They plan to tie the new duct work into the old system prior to the arrival of the new HVAC units that will be located on the roof of the Sunday school addition. The Masonry workers started building the new walls that will enclose the new elevator control room and the mechanical room. The new location for these two rooms is where the old pre-school area is now. The plumbers moved some of the gas lines that are presently running Fellowship Hall to be able to support the new HVAC roof units. They also continued to work on the hot water supply to the front restrooms along with the required drains and venting. The Cement people were here today to pour the floor in the pit of the new elevator. They also covered the plumbing for the new restroom area that the inspector passed last Friday.



Mechanical Room walls and elevator pit poured floor
